




LPG Recovery Plant Civil Works S-Curve

As Of **5-Aug-08**



Description	Progress	Description	Progress	Description	Progress
Cumulative Planned Progress	92.56%	Weekly Planned Progress	0.84%	Cumulative Delta	-18.11%
Cumulative Actual Progress	74.44%	Weekly Actual Progress	2.13%	Weekly Delta	1.28%

Actual to Plan
Accomplish
Cumulative ● 80.43%
Weekly ● 251.96%

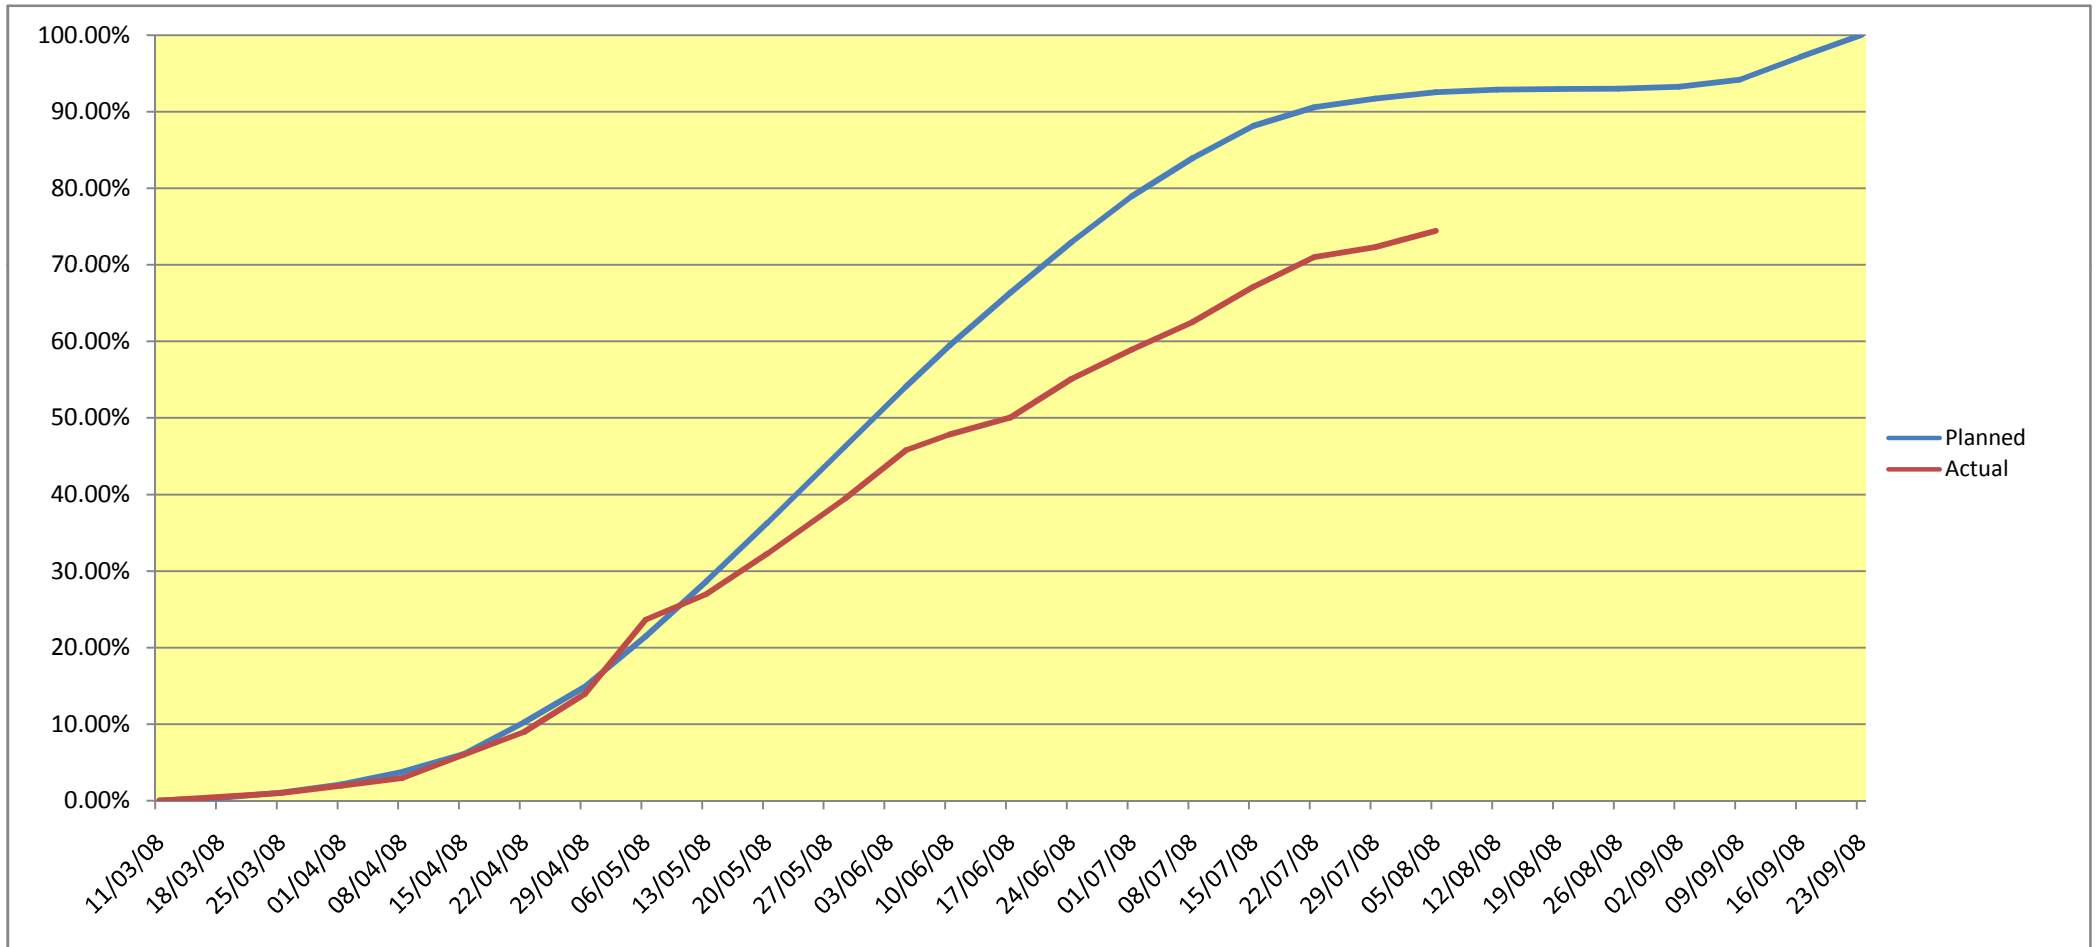

Done by: Eng. Alaa Muneer

KAR Group
